

**BERITA ACARA LAPANGAN (BAL)/
BERITA ACARA PENYELESAIAN PEKERJAAN (BAPP)**

BAL/23/0301

Perbaikan Kabel Fiber Optic, Route kabel dari Simpang jam Ke arah bandara

Supplier Code : VOB-0003
Document Date : 29 November 2023

Purchase Order : PUO/23/0240
Page No. : 1

No.	DESCRIPTION	UOM	BOQ	Realisasi	Keterangan
1.	Galian Vit mengulur kabel fo dari slekan	TITIK	32.00	32.00	
2.	Penarikan fo 48 core duct	MTR	1,730.00	1,730.00	
3.	Instalasi joint closure 48 core	UNT	34.00	34.00	
4.	Splicing kabel FO	COR	1,820.00	1,820.00	
5.	Penarikan Subduct HDPE	MTR	310.00	310.00	
6.	Galian tanah kedalaman 80 cm	MTR	150.00	150.00	

Pekerjaan tersebut telah selesai dilaksanakan dengan hasil yang baik dan sesuai SOP.

Demikian Berita acara ini dibuat, untuk dipergunakan sebagaimana mestinya

Lobam , 29 Nov 2023

PT. Batam Bintang Telekomunikasi

User Mengetahui


Ibrahim


Eddy Naibaho

CITRA INDOTAMA, CV

Vendor,





Mengetahui,



Risna Uli Susanti
Inventori

Menyetujui,



Timbul Nainggolan,
General Manager

IT-GRN.. 23/000.278.....	
Input & Check By	Posted By
	
Risna Uli Susanti	Desmiati M.

Picture 1

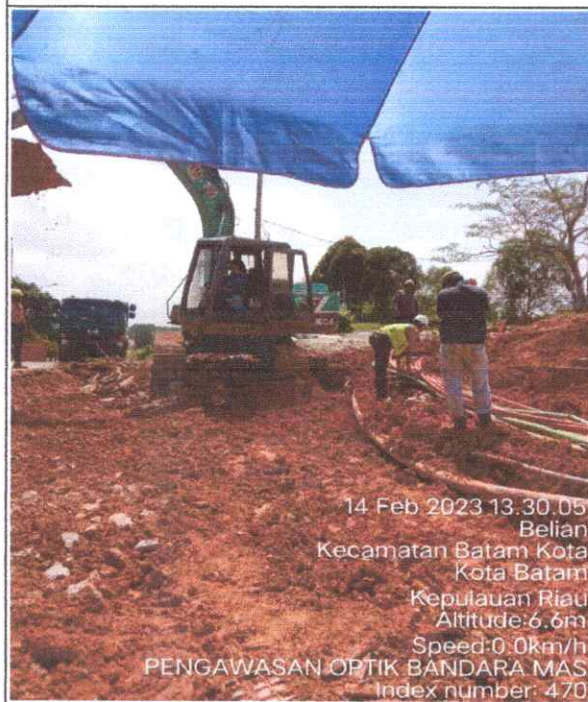

Picture 2

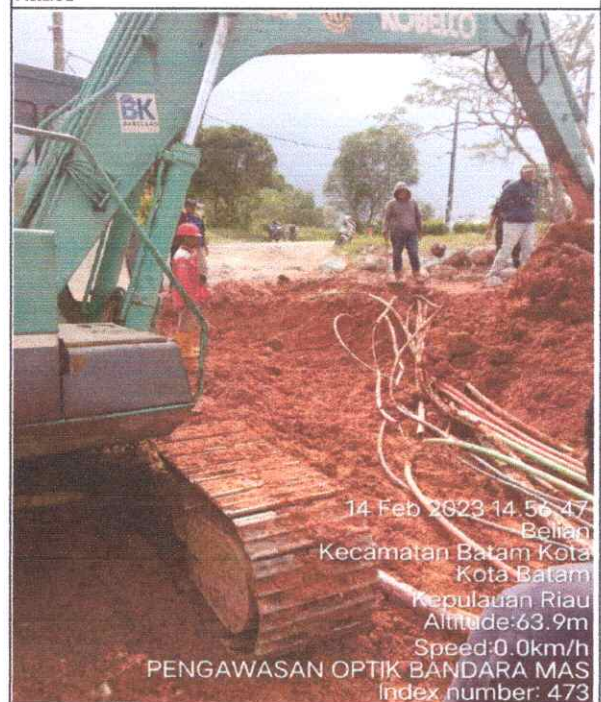

Picture 3



Picture 4



Picture 1



Picture 2



Picture 3



Picture 4




Picture 1




Picture 2




Picture 3

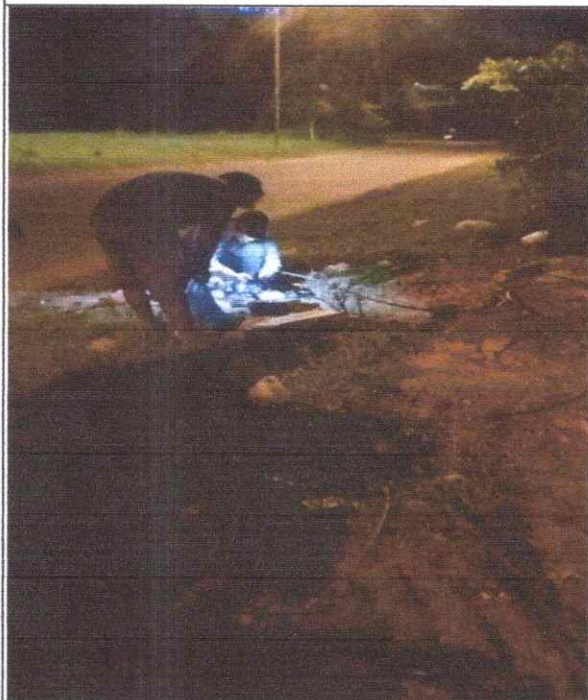


Picture 4

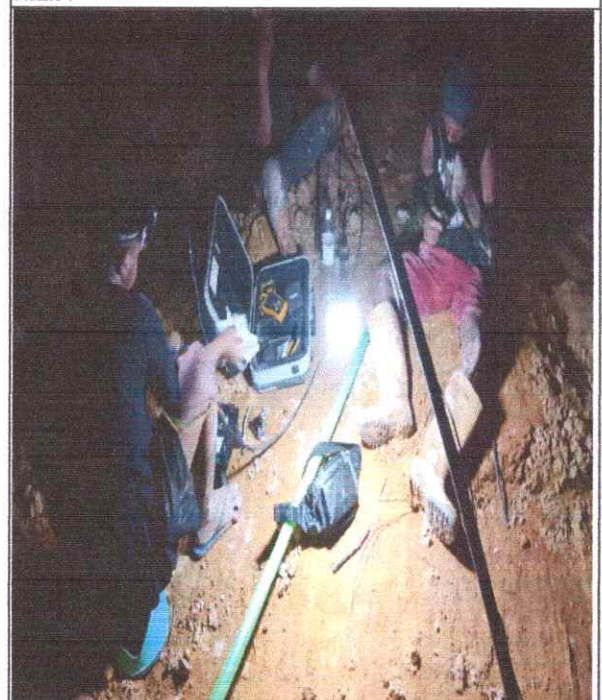


Picture 1

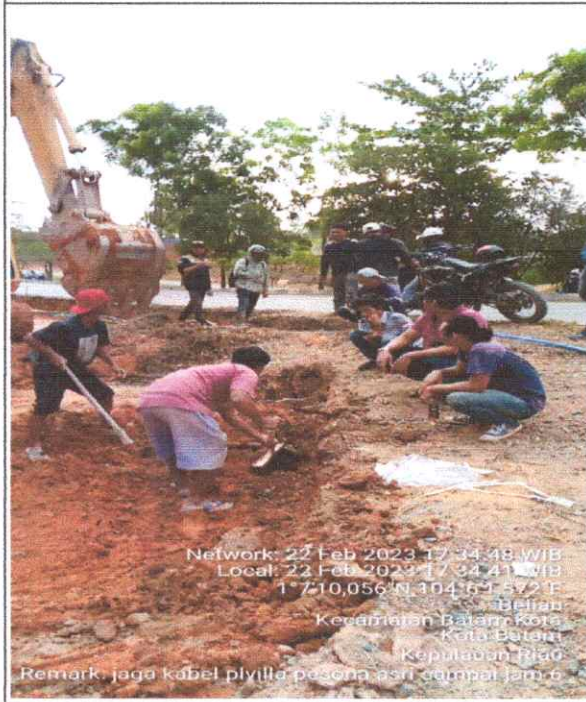


Picture 2

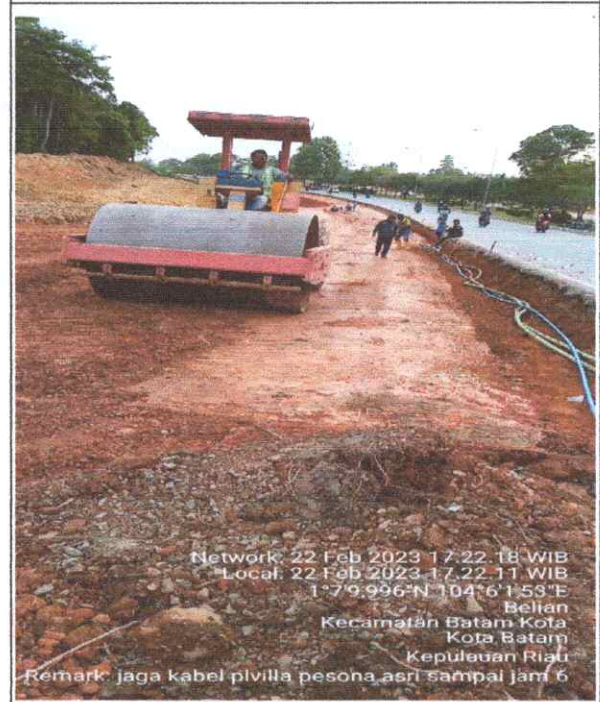

Picture 3

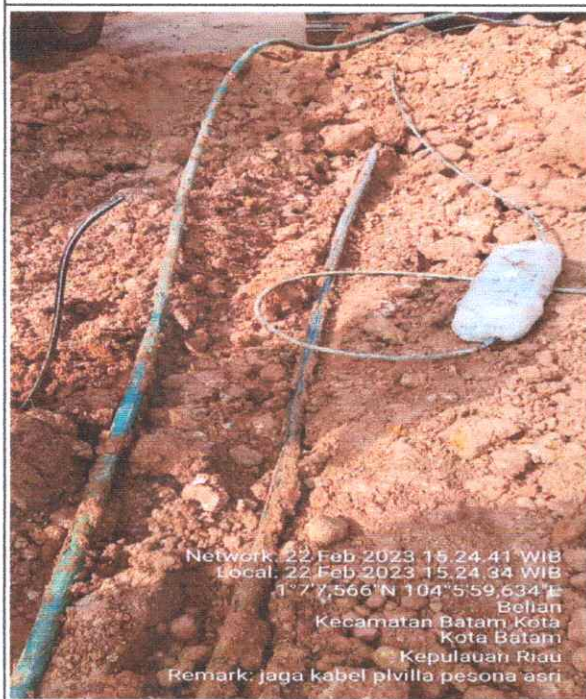


Picture 4

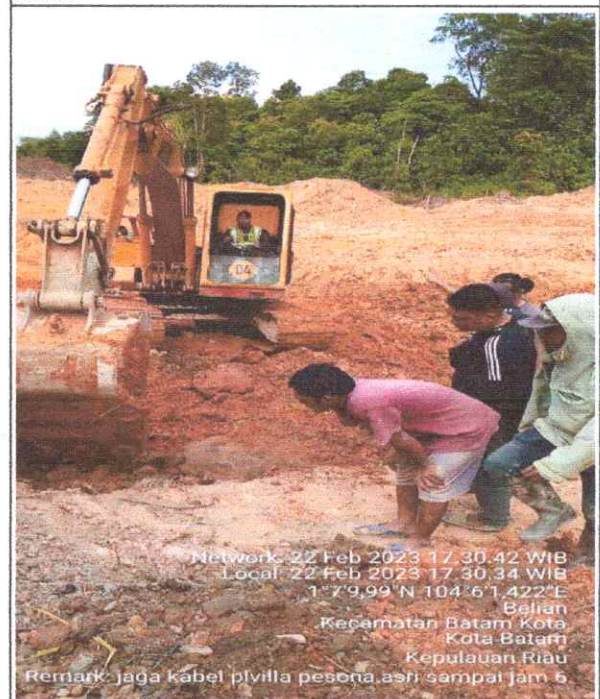

Picture 1




Picture 2

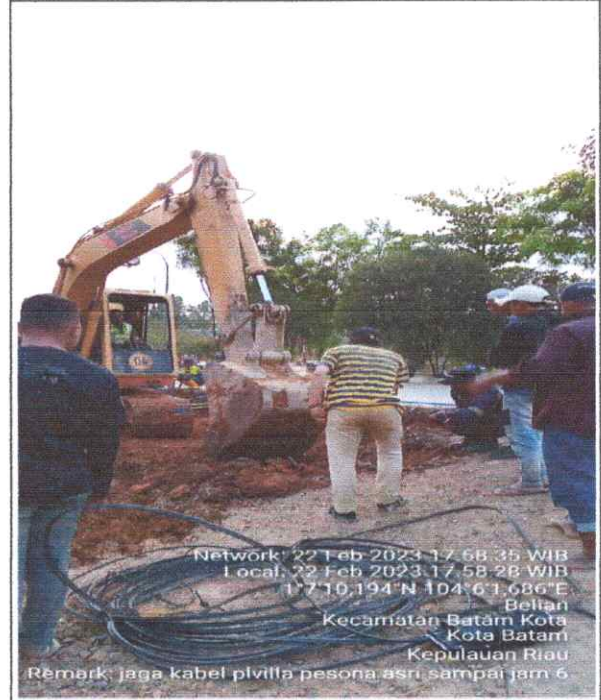

Picture 3




Picture 4

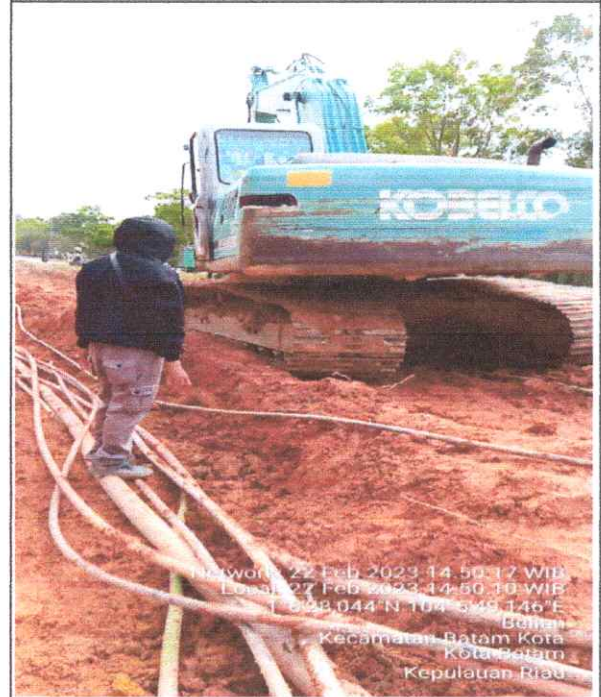

Depan Mega Legenda


Picture 1

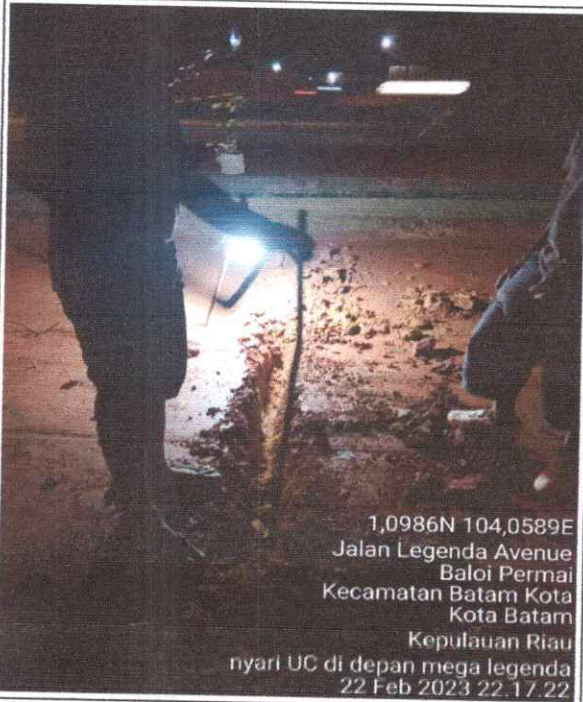


Picture 2



Picture 3

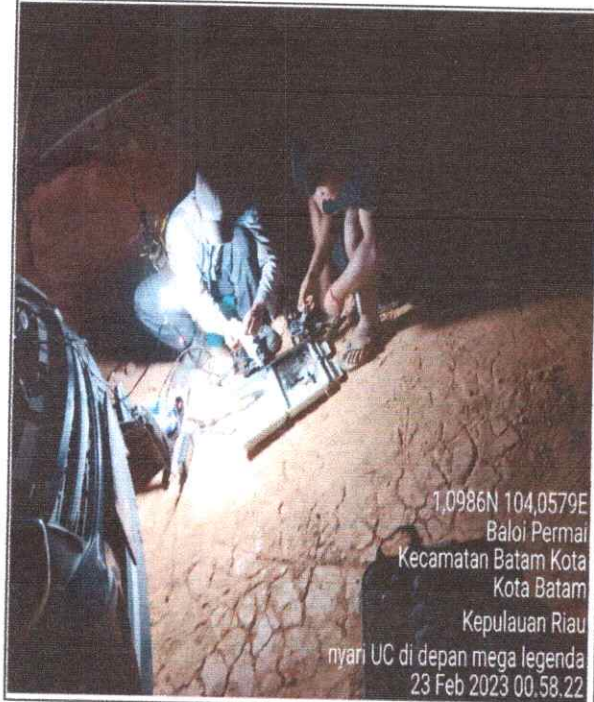

Picture 4

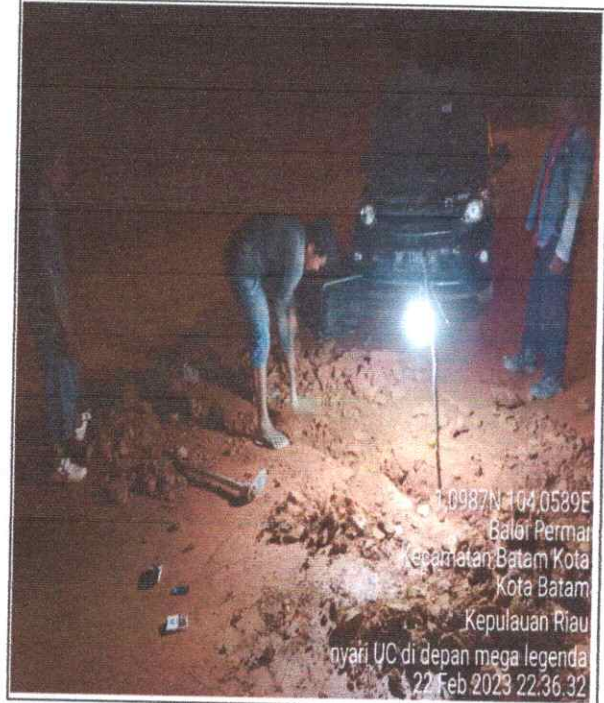


Pasir Putih Batam Center


Picture 1




Picture 2

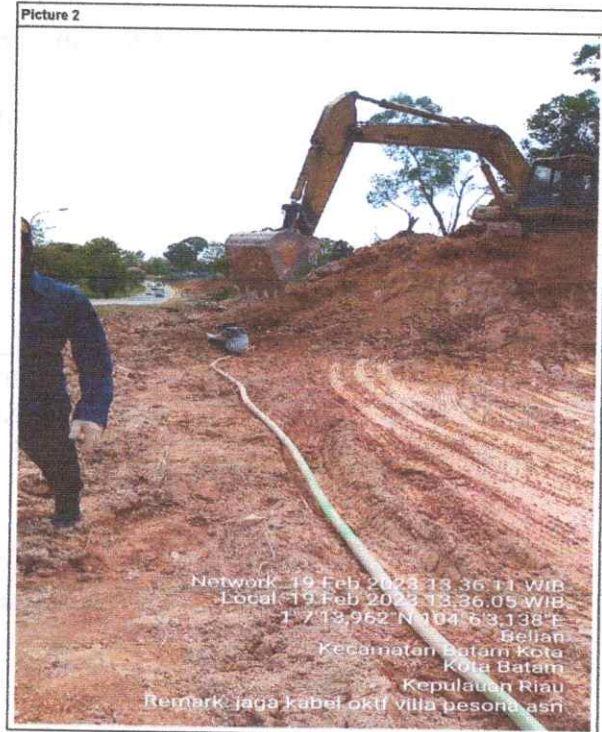


Picture 3

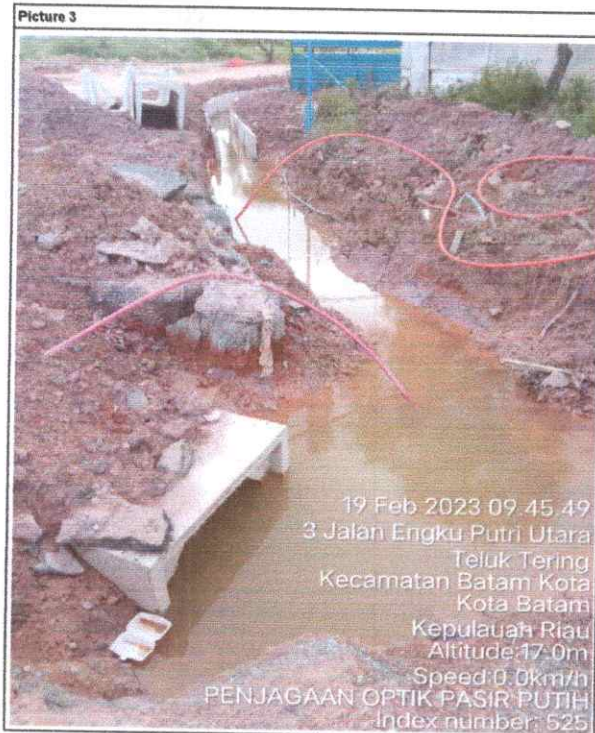



Picture 4

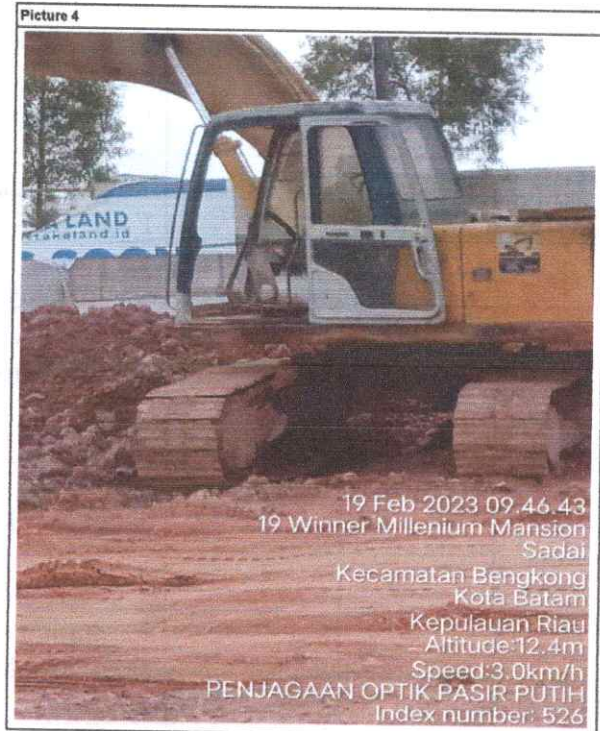


Picture 1

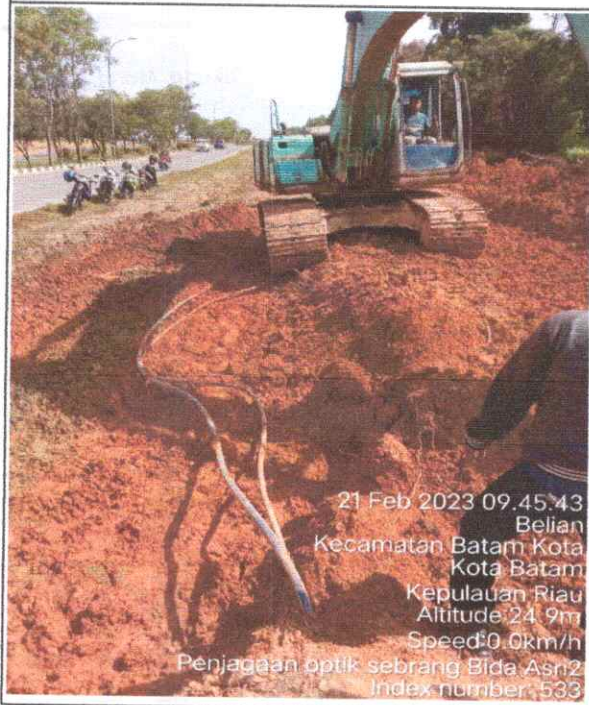


Picture 2

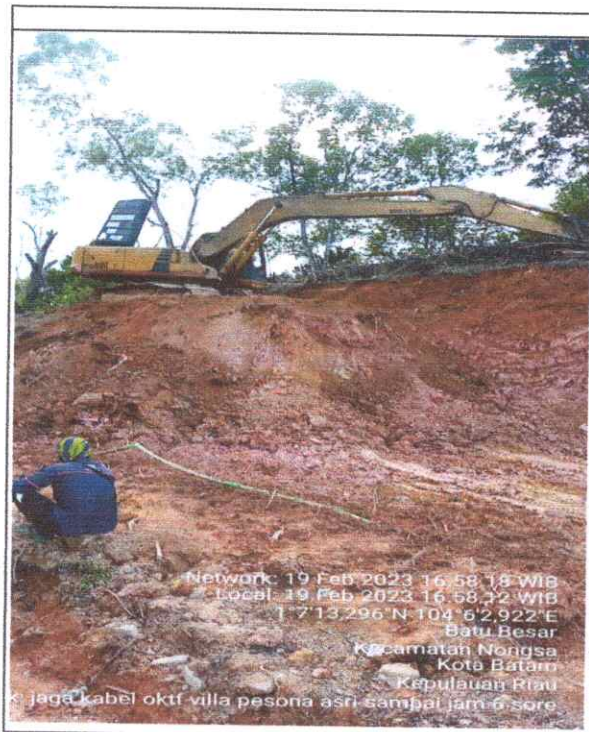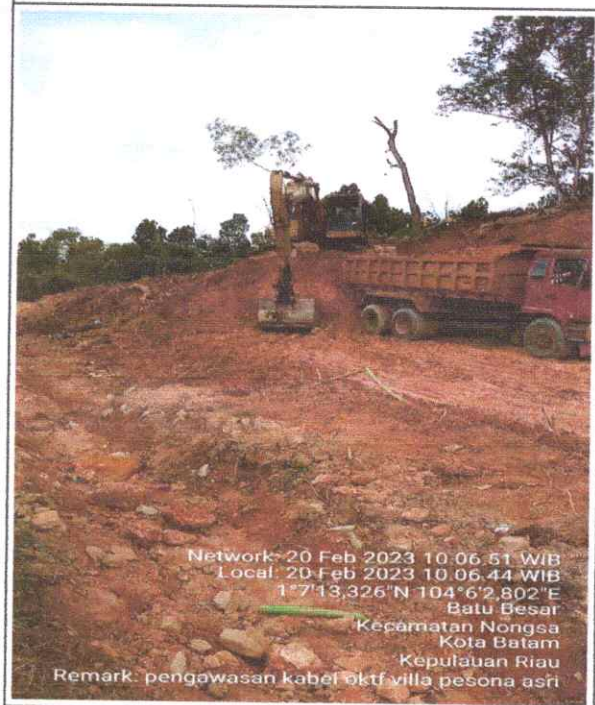


Picture 4

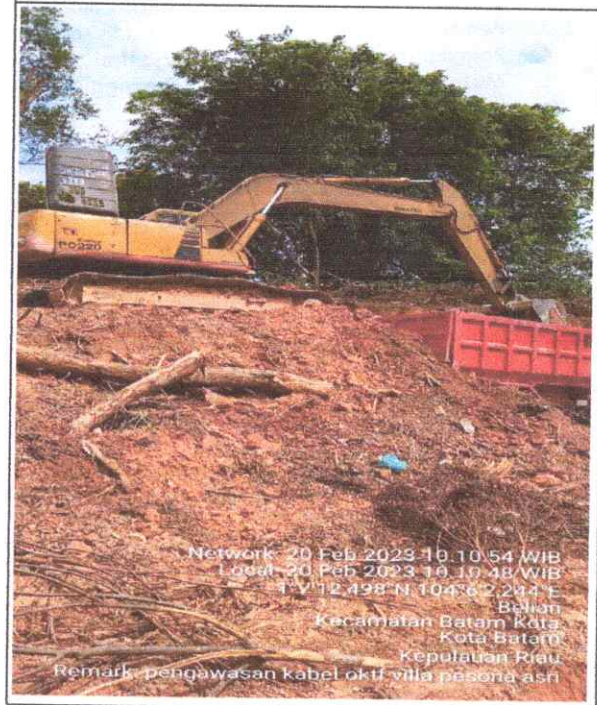

Picture 1

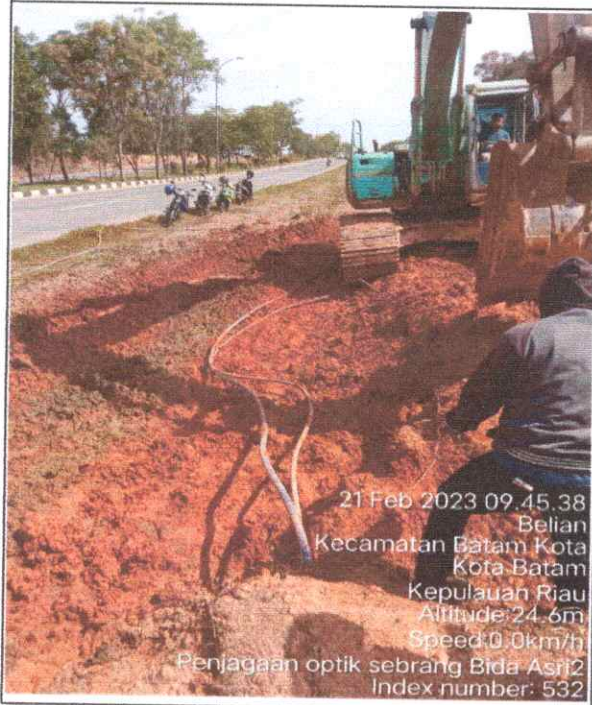


Picture 2

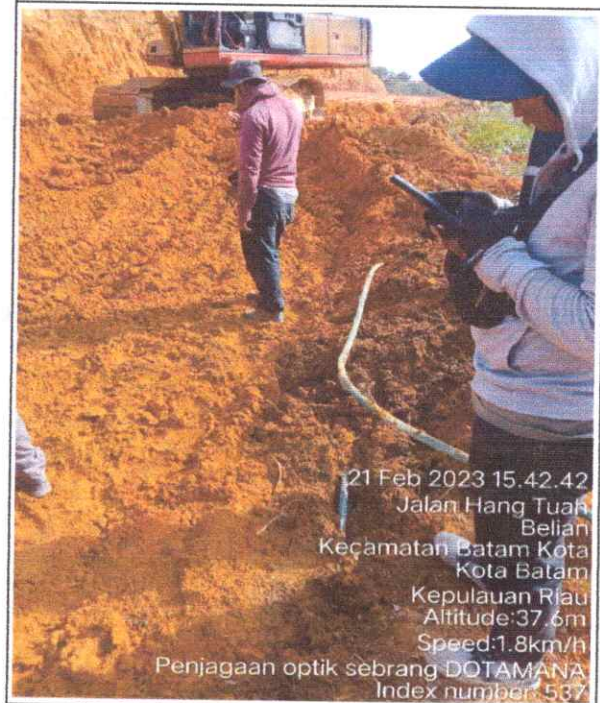


Picture 3



Picture 4

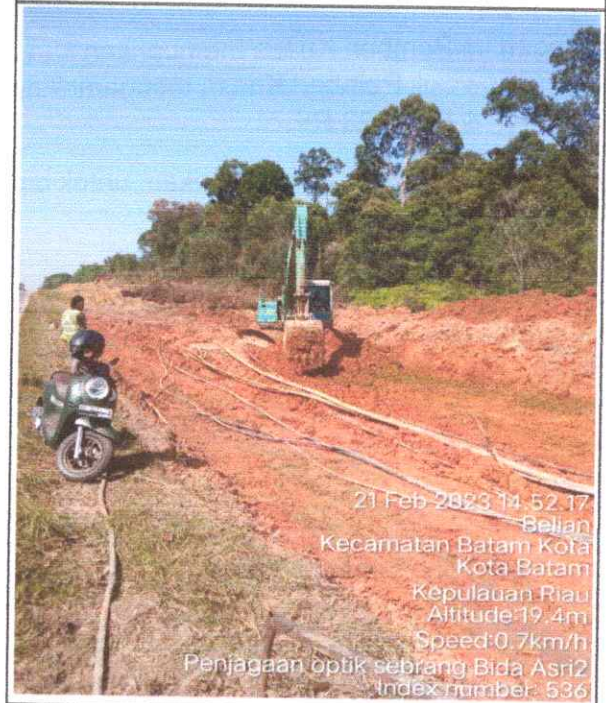

Picture 1

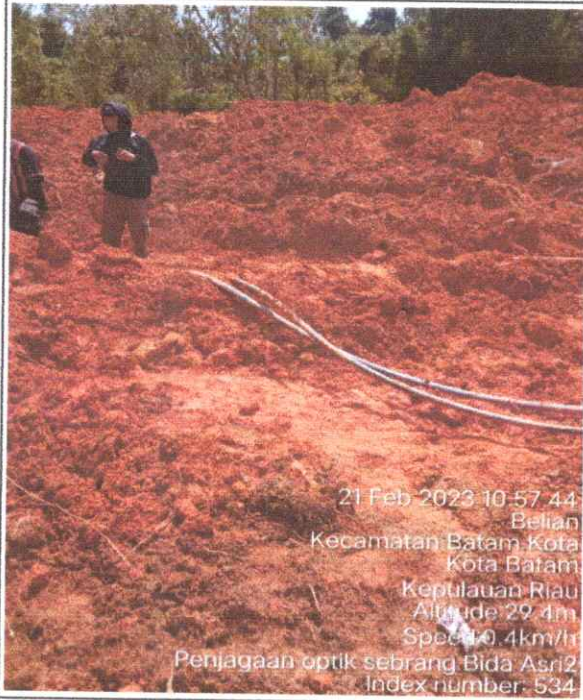


Picture 2




Picture 3




Picture 4

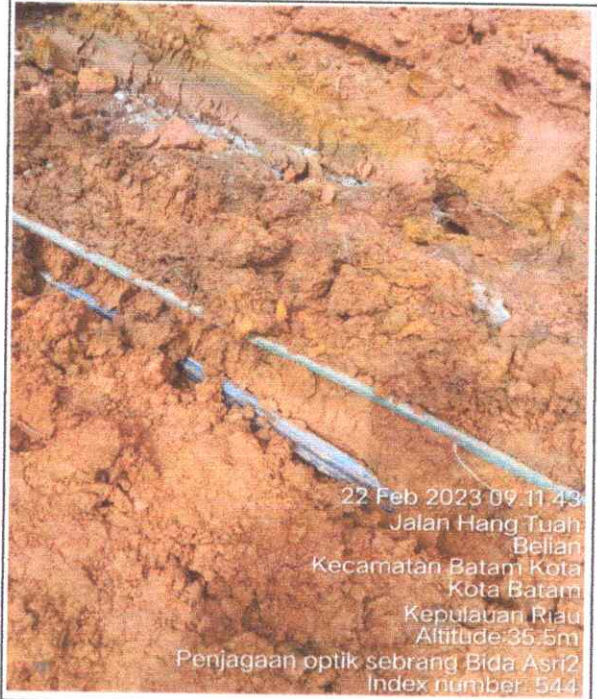

Picture 1

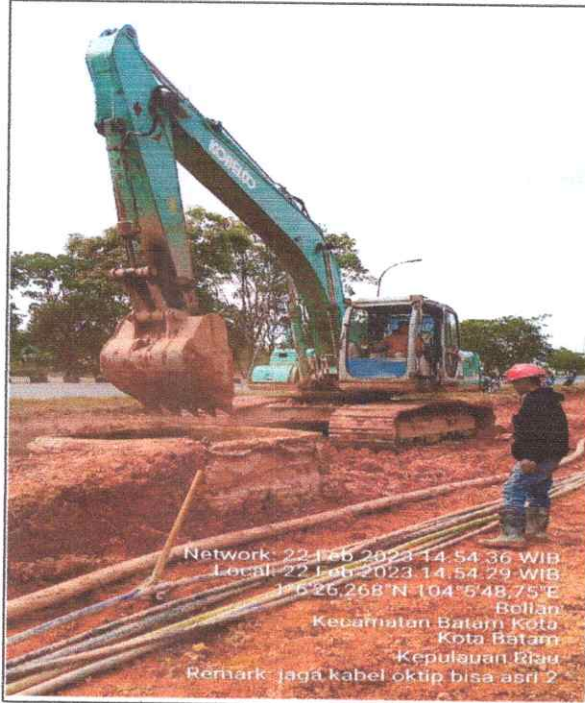


Picture 2

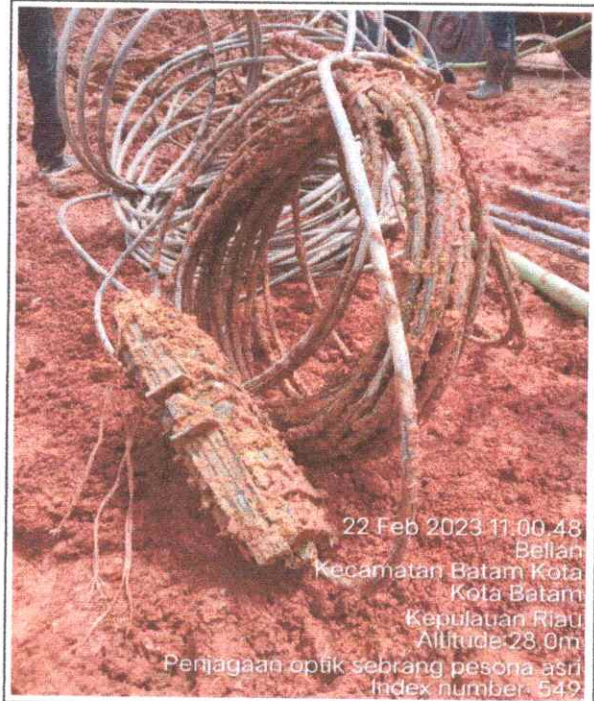

Picture 3




Picture 4

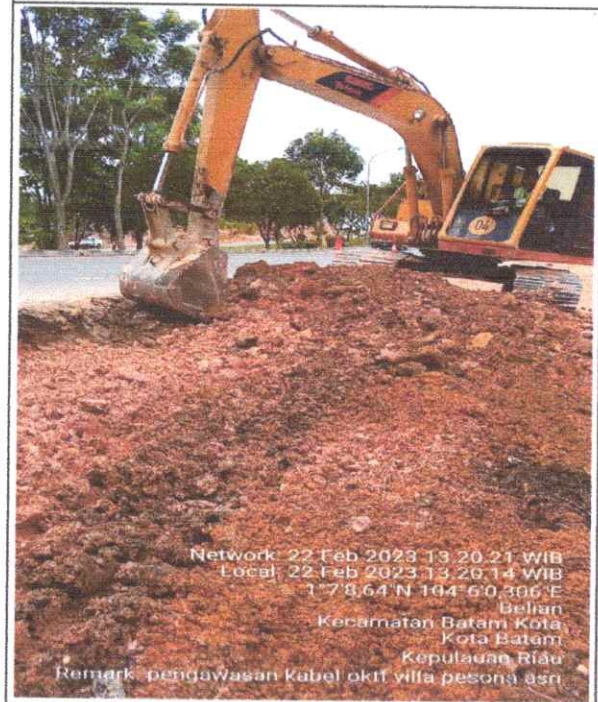

Picture 1



Picture 2

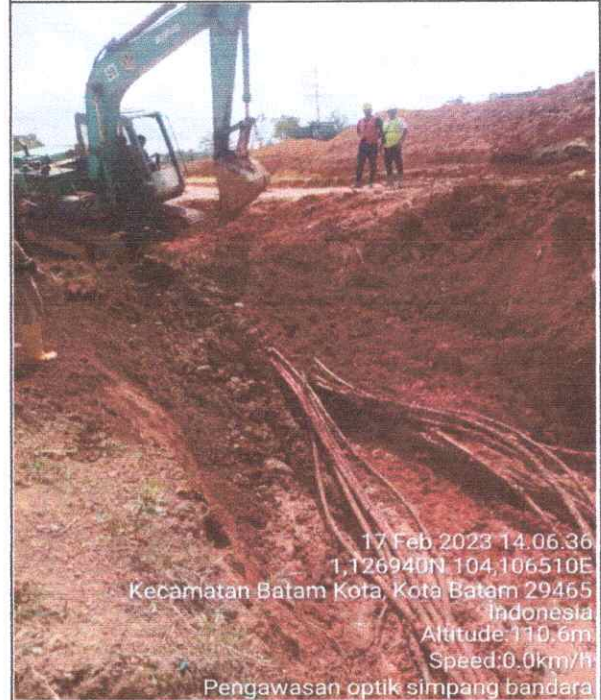


Picture 3




Picture 4



Picture 1

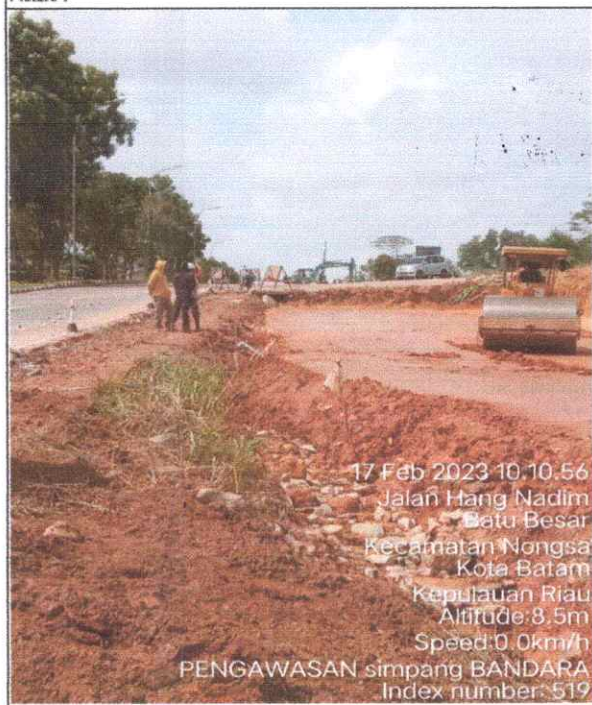


Picture 2

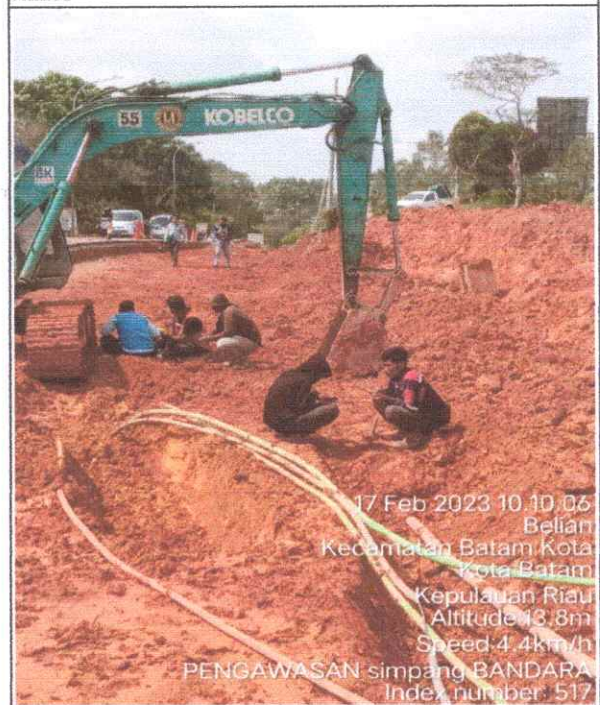


Picture 3




Picture 4

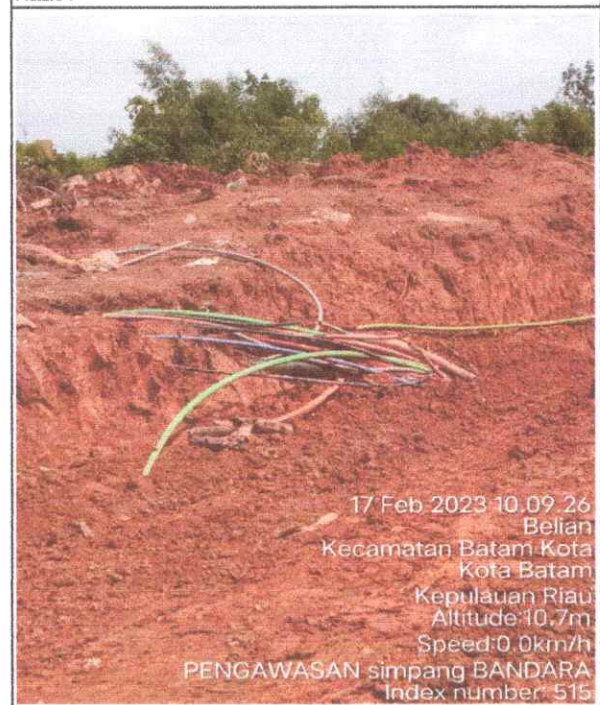


Picture 1

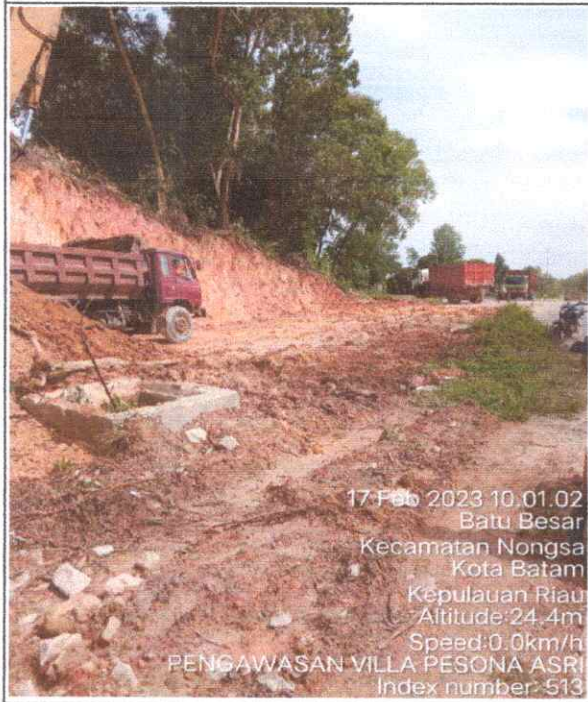


Picture 2

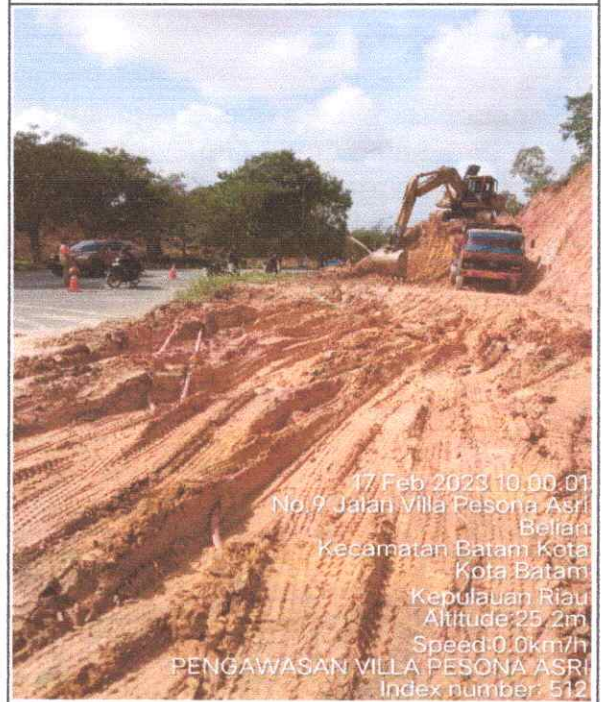


Picture 3

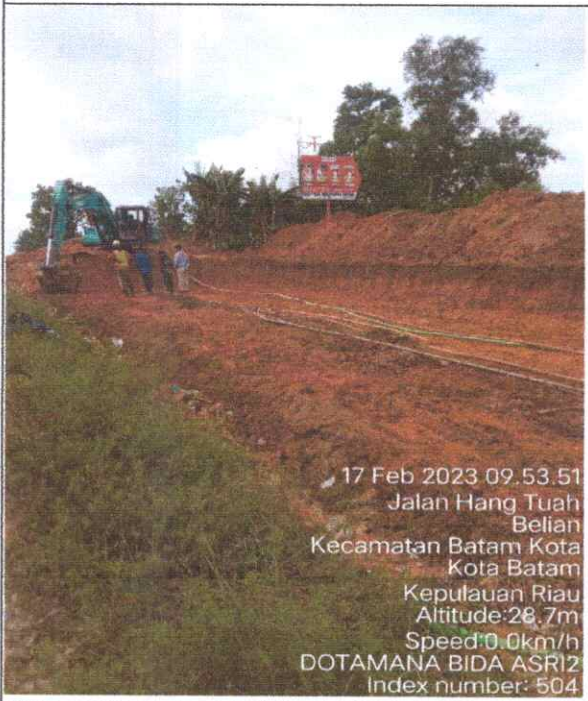

Picture 4

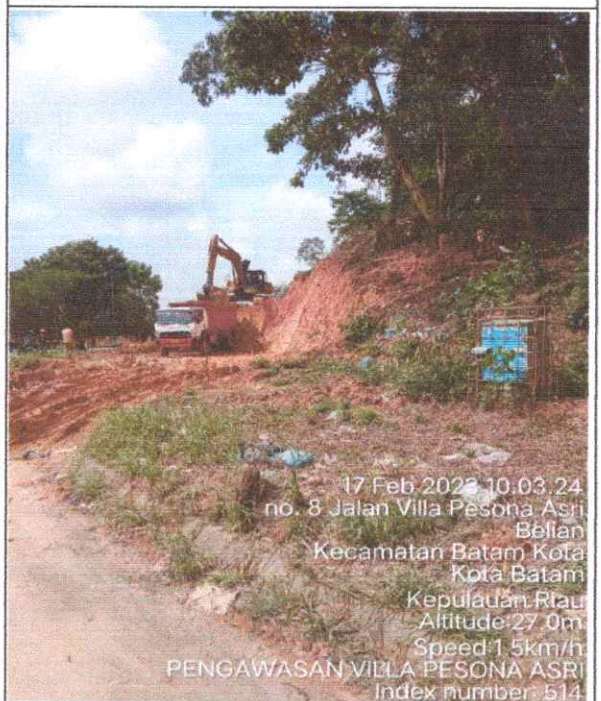


Picture 1

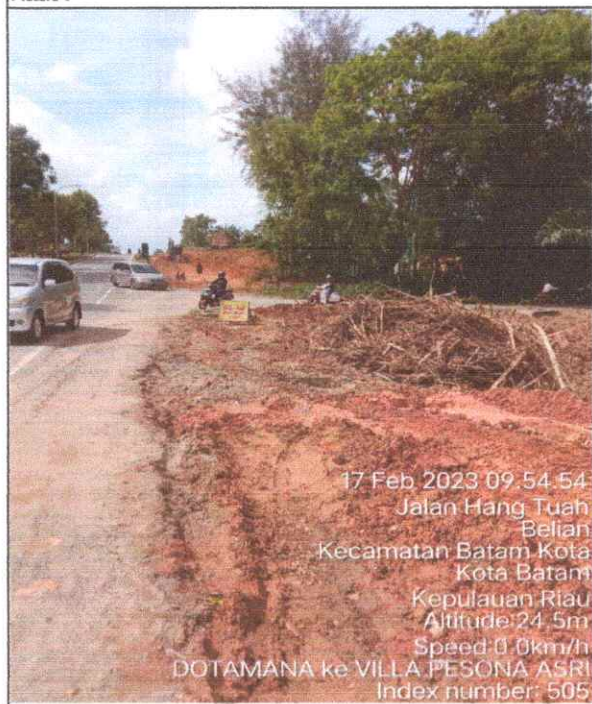


Picture 2



Picture 3

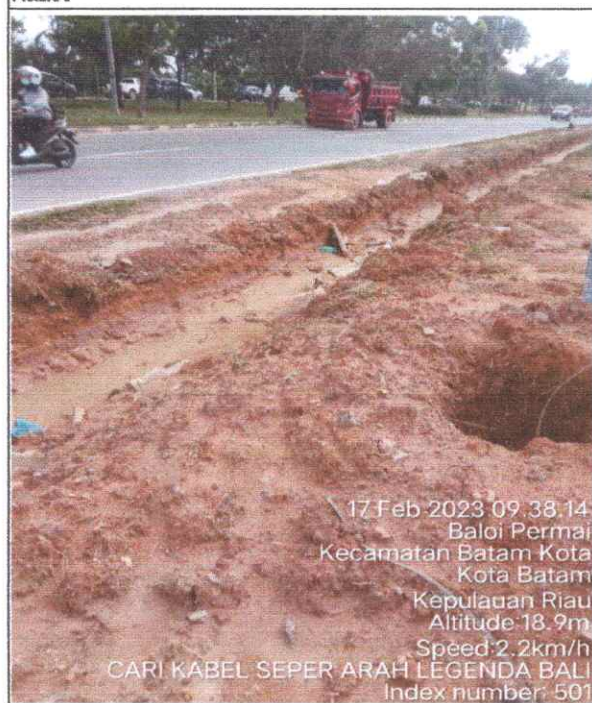


Picture 4

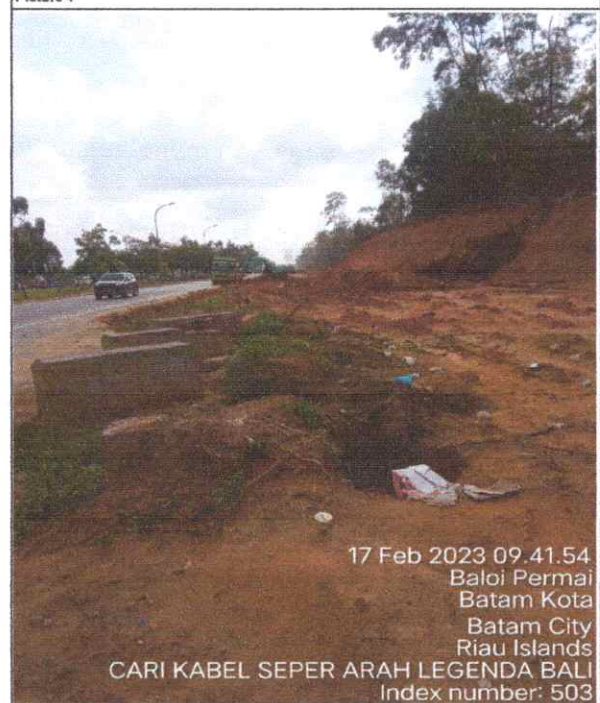


Picture 1



Picture 2

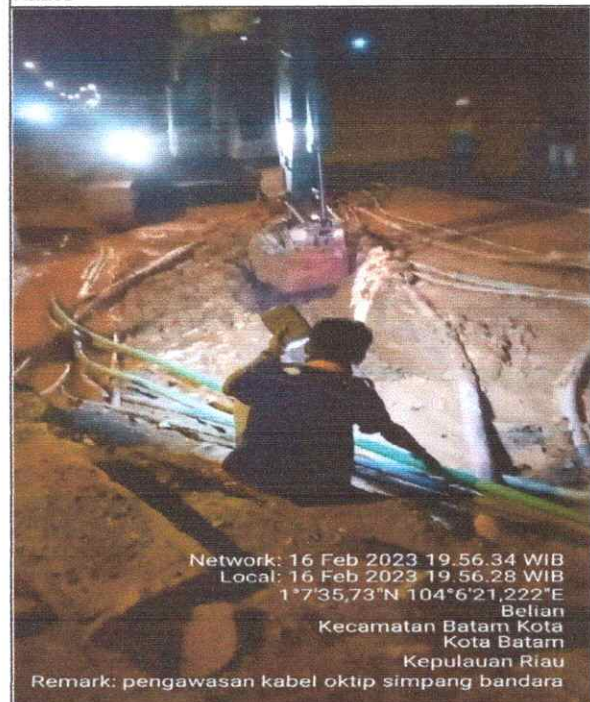


Picture 3




Picture 4




Picture 1

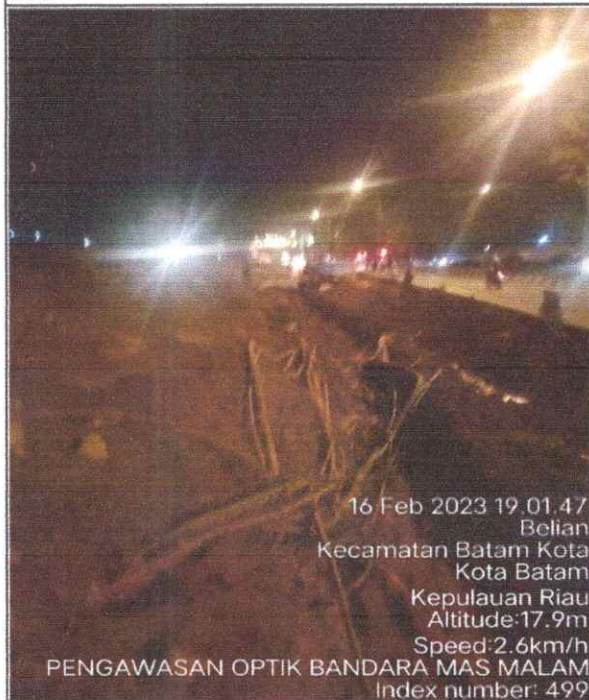


Picture 2

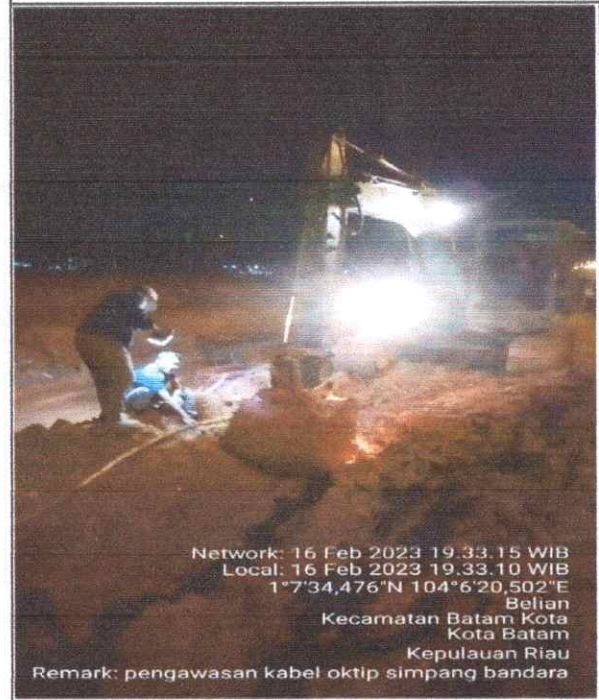

Picture 3

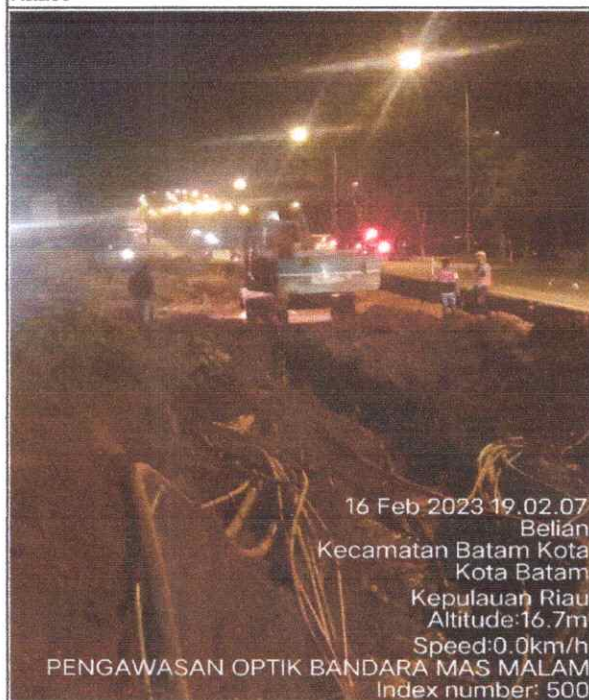


Picture 4

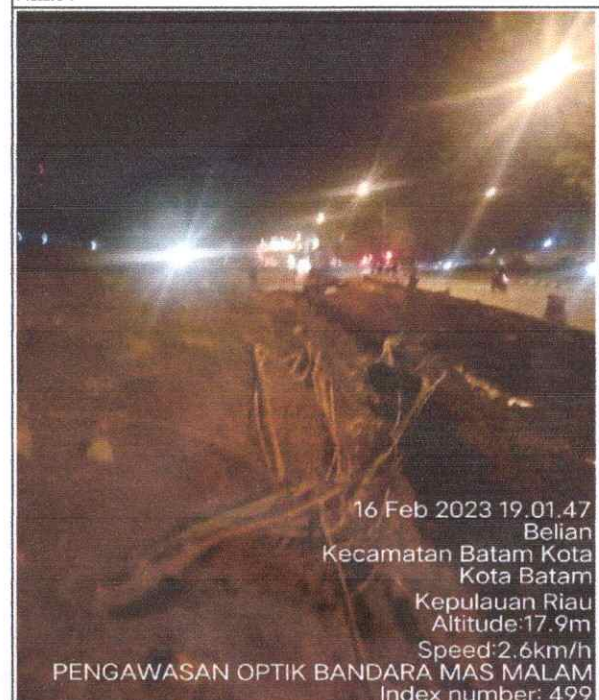


Picture 1




Picture 2

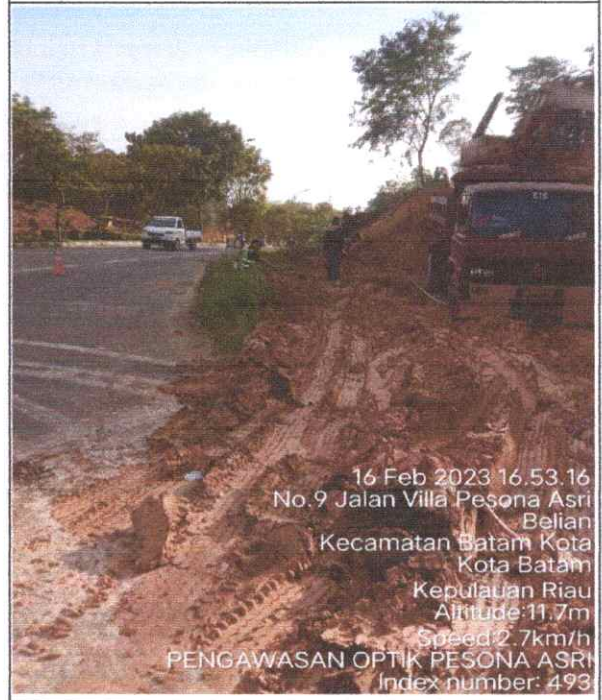

Picture 3

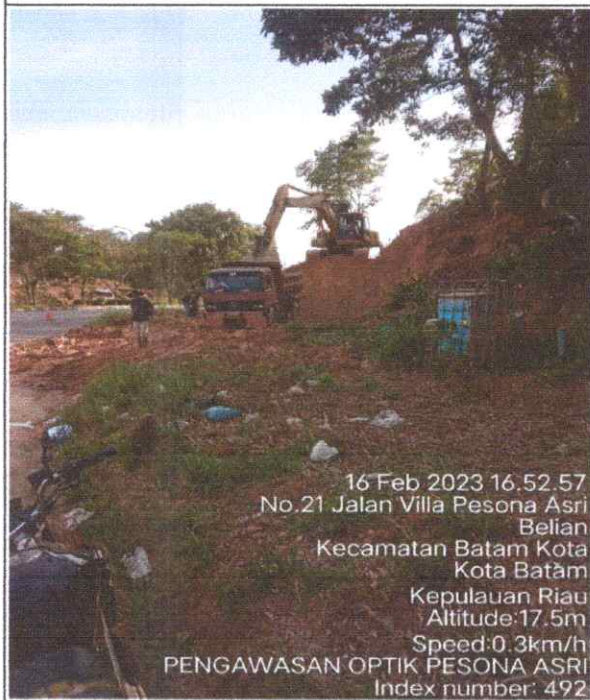


Picture 4

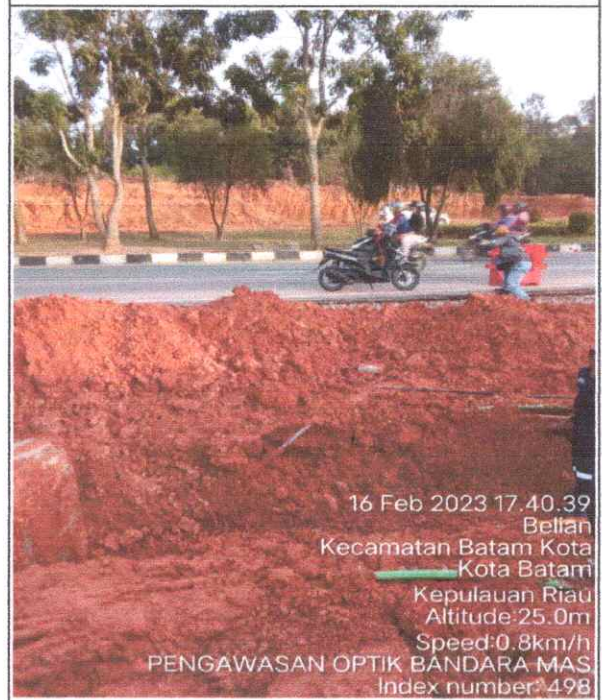

Picture 1



Picture 2

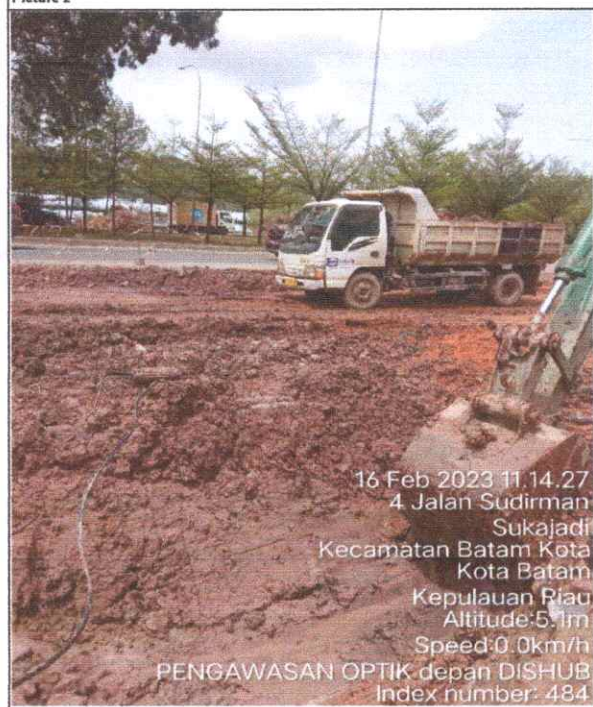

Picture 3



Picture 4

